

1



LEVEL SITE

2




FOOTINGS

3




MAIN DRAIN INSTALL


4



HOTEL ROOMS




SERVICE CORE





RECEPTION, STAIRS

ERECT EXTERNAL & INTERNAL PRECAST WALLS & ROOF SLABS (EXCEPT OVER STAIR WELL)

5

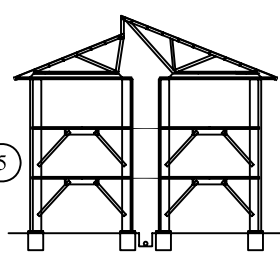


ERECT ROOF TRUSS UNITS, INSULATION & SHEETING.
TEMP FORMWORK UNITS, PRECAST FLOOR SLABS & CONDECK
PLUMBING & ELECTRICAL "ROUGH IN", REINFORCING TO 1ST & 2ND FLOOR SLABS.

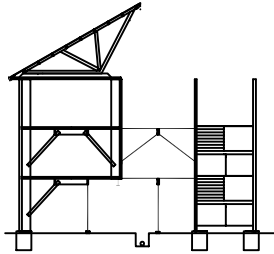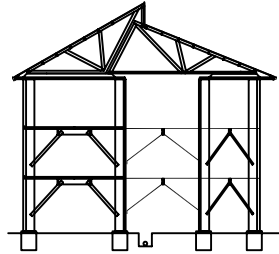


PRECAST STAIRS


6

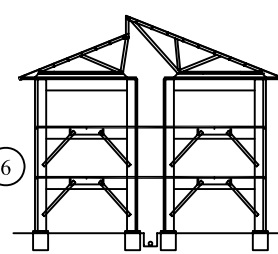

POUR UPPER FLOOR SLABS
FIX TOP PRECAST LIGHTWEIGHT
WALL PANELS

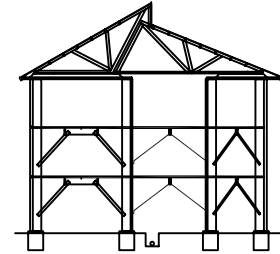


GROUND FLOOR DRAINAGE
"ROUGH IN".

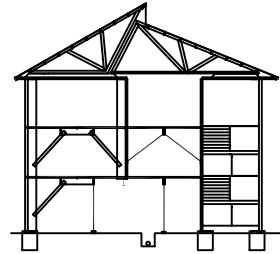


FIX PRECAST ROOF SLAB, TRUSS
UNITS & ROOFING OVER
STAIR WELL.


7

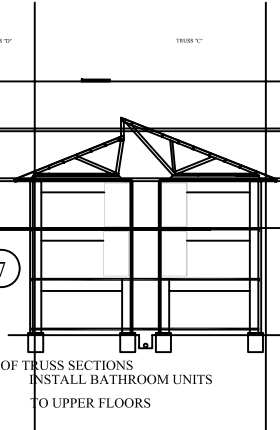

ROOF TRUSS SECTIONS
INSTALL BATHROOM UNITS
TO UPPER FLOORS

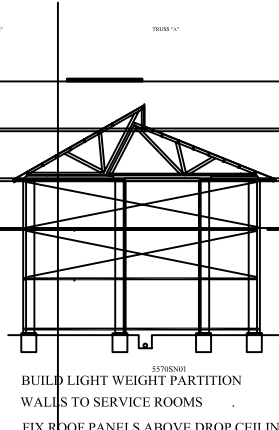


BUILD LIGHT WEIGHT PARTITION
WALLS TO SERVICE ROOMS
FIX ROOF PANELS ABOVE DROP CEILING.

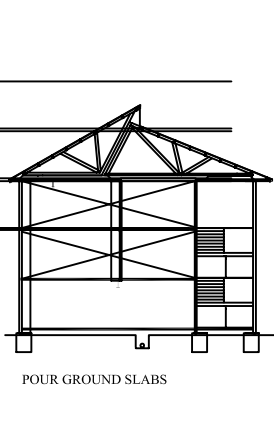


POUR GROUND SLABS


8



FIX PRECAST END WALLS
FIX END PRECAST ROOF PANELS




FIX PREFAB GABLE ENDS
FIT END PASSAGE DOORS




SEAL JOINTS BETWEEN WALLS
EXTERNAL SITE WORKS


9

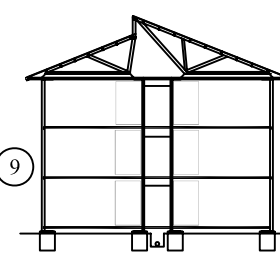

COMPLETE GROUND FLOOR
FIX ROOF PANELS ABOVE CORRIDOR
COMPLETE ROOMS & FITOUT

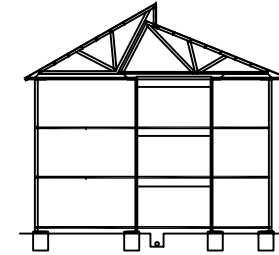

INSTALL FALSE CEILINGS

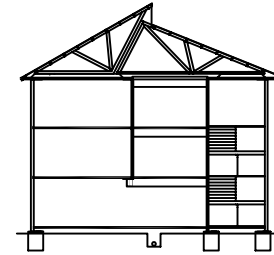

FIREPROOF RSJ

copyright

PROPOSED CONSTRUCTION SEQUENCE

5572C
UNIBUILD
www.unibuild.com
